


KAYNAK DENGEME

Task Name	Duration	Start	Finish	Work	Predecessors	Resource Names
A	20 days	Fri 28.05.10	Thu 24.06.10	320 hrs		Kerem;Ahmet
B	20 days	Fri 25.06.10	Thu 22.07.10	240 hrs	1	Necati[50%];Kerem
C	20 days	Fri 16.07.10	Thu 12.08.10	320 hrs	2FS-5 days	Fatih;Kerem
D	20 days	Fri 25.06.10	Thu 22.07.10	240 hrs	1	Taner;Kerem[50%]
E	20 days	Fri 13.08.10	Thu 09.09.10	480 hrs	3;4	Okyay;Necati;Kerem
F	0 days	Thu 09.09.10	Thu 09.09.10	0 hrs	5	Ahmet

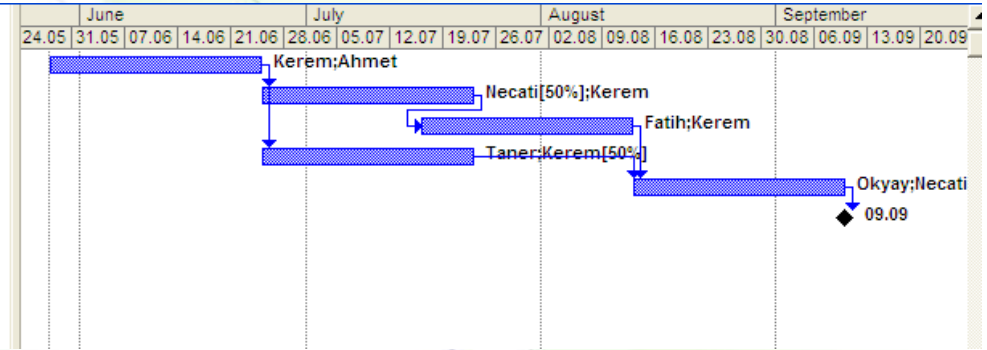

Resource Name	Work	Details	June					July					August				September	
			24.05	31.05	07.06	14.06	21.06	28.06	05.07	12.07	19.07	26.07	02.08	09.08	16.08	23.08	30.08	06.09
<input checked="" type="checkbox"/> Kerem	720 hrs	Work	8h	40h	40h	40h	44h	60h	60h	68h	88h	40h	40h	40h	40h	40h	40h	32h
A	160 hrs	Work	8h	40h	40h	40h	32h											
B	160 hrs	Work					8h	40h	40h	40h	32h							
C	160 hrs	Work							8h	40h	40h	40h	32h					
D	80 hrs	Work					4h	20h	20h	20h	16h							
E	160 hrs	Work												8h	40h	40h	40h	32h
<input checked="" type="checkbox"/> Necati	240 hrs	Work					4h	20h	20h	20h	16h			8h	40h	40h	40h	32h
B	80 hrs	Work					4h	20h	20h	20h	16h							
E	160 hrs	Work												8h	40h	40h	40h	32h
<input checked="" type="checkbox"/> Fatih	160 hrs	Work							8h	40h	40h	40h	32h					
C	160 hrs	Work							8h	40h	40h	40h	32h					
<input checked="" type="checkbox"/> Taner	160 hrs	Work					8h	40h	40h	40h	32h							
D	160 hrs	Work					8h	40h	40h	40h	32h							
<input checked="" type="checkbox"/> Okyay	160 hrs	Work												8h	40h	40h	40h	32h
E	160 hrs	Work												8h	40h	40h	40h	32h
<input checked="" type="checkbox"/> Ahmet	160 hrs	Work	8h	40h	40h	40h	32h											0h
A	160 hrs	Work	8h	40h	40h	40h	32h											0h
F	0 hrs	Work																0h
		Work																0h

KAYNAK DENGEME

Resource Name	Work	Details	June					July					August					September	
			24.05	31.05	07.06	14.06	21.06	28.06	05.07	12.07	19.07	26.07	02.08	09.08	16.08	23.08	30.08	06.09	13
<input checked="" type="checkbox"/> Kerem	640 hrs	Work	8h	40h	40h	40h	40h	40h	48h	72h	40h	40h	40h	40h	40h	40h	40h	32h	
A	160 hrs	Work	8h	40h	40h	40h	32h												
B	160 hrs	Work					8h	40h	40h	40h	32h								
C	160 hrs	Work							8h	40h	40h	40h	32h						
E	160 hrs	Work												8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Necati	320 hrs	Work					8h	40h	40h	40h	32h			8h	40h	40h	40h	32h	
B	80 hrs	Work					4h	20h	20h	20h	16h								
D	80 hrs	Work					4h	20h	20h	20h	16h								
E	160 hrs	Work												8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Fatih	160 hrs	Work							8h	40h	40h	40h	32h						
C	160 hrs	Work							8h	40h	40h	40h	32h						
<input checked="" type="checkbox"/> Taner	120 hrs	Work					8h	40h	40h	32h									
D	120 hrs	Work					8h	40h	40h	32h									
<input checked="" type="checkbox"/> Okyay	160 hrs	Work												8h	40h	40h	40h	32h	
E	160 hrs	Work												8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Ahmet	160 hrs	Work	8h	40h	40h	40h	32h												0h
A	160 hrs	Work	8h	40h	40h	40h	32h												
F	0 hrs	Work																	0h
		Work																	

Kerem D aktivitesinden çıkarken, Necati D aktivitesine atandı.

KAYNAK DENGEME

Resource Name	Work	Details	June				July				August				September			
			24.05	31.05	07.06	14.06	21.06	28.06	05.07	12.07	19.07	26.07	02.08	09.08	16.08	23.08	30.08	06.09
<input checked="" type="checkbox"/> Kerem	480 hrs	Work	8h	40h	40h	40h	40h	40h	40h	40h	32h			8h	40h	40h	40h	32h
A	160 hrs	Work	8h	40h	40h	40h	32h											
B	160 hrs	Work					8h	40h	40h	40h	32h							
E	160 hrs	Work											8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Necati	320 hrs	Work					8h	40h	40h	40h	32h		8h	40h	40h	40h	32h	
B	80 hrs	Work					4h	20h	20h	20h	16h							
D	80 hrs	Work					4h	20h	20h	20h	16h							
E	160 hrs	Work											8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Fatih	160 hrs	Work							8h	40h	40h	40h	32h					
C	160 hrs	Work							8h	40h	40h	40h	32h					
<input checked="" type="checkbox"/> Taner	120 hrs	Work					8h	40h	40h	32h								
D	120 hrs	Work					8h	40h	40h	32h								
<input checked="" type="checkbox"/> Okyay	160 hrs	Work											8h	40h	40h	40h	32h	
E	160 hrs	Work											8h	40h	40h	40h	32h	
<input checked="" type="checkbox"/> Ahmet	320 hrs	Work	8h	40h	40h	40h	32h		8h	40h	40h	40h	32h				0h	
A	160 hrs	Work	8h	40h	40h	40h	32h											
C	160 hrs	Work							8h	40h	40h	40h	32h					
F	0 hrs	Work															0h	
		Work																

Kerem C aktivitesinden çıkarırken, Ahmet C aktivitesine atandı.
